ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	✓	**Mill Valley Middle School ADA**	**168 days**	**Thu 1/28/10**	**Fri 9/17/10**		
2	✓	**District Programming**	**20 days**	**Mon 3/1/10**	**Fri 3/26/10**		
3	✓	Procure Soils Report	20 days	Mon 3/1/10	Fri 3/26/10		
4	✓	Procure Special Testi	20 days	Mon 3/1/10	Fri 3/26/10		
5	✓	Procure Project Inspe	20 days	Mon 3/1/10	Fri 3/26/10		
6	✓	**Schematic Design**	**22 days**	**Thu 1/28/10**	**Fri 2/26/10**		
7	✓	Develop Schematic D	22 days	Thu 1/28/10	Fri 2/26/10		
8	✓	**Construction Documents**	**19 days**	**Tue 3/2/10**	**Fri 3/26/10**		
9	✓	Develop Construction	19 days	Tue 3/2/10	Fri 3/26/10		
10	✓	**Agency Approval**	**42 days**	**Mon 3/1/10**	**Tue 4/27/10**		
11	✓	Preliminary DSA Revi	1 day	Mon 3/1/10	Mon 3/1/10	7	
12	✓	DSA Review& Approv	22 days	Mon 3/29/10	Tue 4/27/10	9	
13	✓	PM/CM Constructabili	10 days	Mon 3/29/10	Fri 4/9/10		
14	✓	**Pre-Construction Activiti**	**30 days**	**Tue 4/27/10**	**Mon 6/7/10**		
15	✓	Advertisement Numbe	5 days	Tue 4/27/10	Mon 5/3/10		
16	✓	Advertisement Numbe	5 days	Mon 5/3/10	Fri 5/7/10		
17	✓	Pre-bid Conference	1 day	Thu 4/29/10	Thu 4/29/10		
18	✓	Bid Period	1 day	Thu 5/13/10	Thu 5/13/10		
19	✓	Bid Review & Award	1 day	Mon 6/7/10	Mon 6/7/10	18	
20	✓	**Construction Period**	**66 days**	**Mon 6/21/10**	**Fri 9/17/10**		
21	✓	Notice to Proceed	1 day	Mon 6/21/10	Mon 6/21/10		
22	✓	Construction Period	46 days	Mon 6/21/10	Fri 8/20/10	21	
23	✓	Closeout	20 days	Mon 8/23/10	Fri 9/17/10	22	
24							
25		**Edna Maguire Elementary Scl**	**1015 days**	**Thu 2/11/10**	**Tue 12/31/13**		
26	✓	**District Programming**	**178 days**	**Thu 2/11/10**	**Fri 10/15/10**		
27	✓	Kick -off Meeting with	1 day	Wed 2/24/10	Wed 2/24/10		
28	✓	Ed. Spec review meet	1 day	Thu 2/11/10	Thu 2/11/10		
29	✓	Develop Design Comr	22 days	Thu 2/25/10	Fri 3/26/10		
30	✓	Procure Professional S	57 days	Thu 2/25/10	Fri 5/14/10		
31	✓	Procure Professional S	22 days	Thu 2/25/10	Fri 3/26/10		
32	✓	Commence CEQA	121 days	Mon 5/3/10	Fri 10/15/10		
33	✓	**Schematic Design**	**146 days**	**Mon 4/5/10**	**Fri 10/22/10**		
34	✓	Adopt Prequalification	40 days	Sun 8/1/10	Thu 9/23/10		
35	✓	Develop Schematic D	121 days	Mon 4/5/10	Fri 9/17/10		
36	✓	District Review & Appr	25 days	Mon 9/20/10	Fri 10/22/10	35	
37	✓	**Design Development**	**78 days**	**Mon 10/25/10**	**Wed 2/9/11**		
38	✓	Develop DD Documer	48 days	Mon 10/25/10	Wed 12/29/10	36	
39	✓	District Review & Appr	30 days	Thu 12/30/10	Wed 2/9/11	38	
40	✓	**Construction Documents**	**138 days**	**Thu 2/10/11**	**Mon 8/22/11**		
41	✓	Develop 50% CD Doc	55 days	Thu 2/10/11	Wed 4/27/11	39	
42	✓	District Review & Appr	15 days	Thu 4/28/11	Wed 5/18/11	41	
43	✓	Develop 100% CD Do	43 days	Thu 5/19/11	Mon 7/18/11	42	
44	✓	District Review & Appr	25 days	Tue 7/19/11	Mon 8/22/11	43	
45		**Agency Approval**	**372 days**	**Mon 10/18/10**	**Tue 3/20/12**		
46	✓	Finalize CEQA	166 days	Mon 10/18/10	Mon 6/6/11	32	
47	✓	CDE Approval	20 days	Tue 6/7/11	Mon 7/4/11	46	
48		DSA Approval	110 days	Thu 9/1/11	Wed 2/1/12	44FS+7 days	
49		PM/CM Constructabili	110 days	Tue 8/23/11	Mon 1/23/12	44	
50		Incorporate PM/CM &	10 days	Tue 1/24/12	Mon 2/6/12	49	
51		DSA Backcheck	30 days	Tue 2/7/12	Mon 3/19/12	50	
52		Final DSA Approval	1 day	Tue 3/20/12	Tue 3/20/12	51	
53		**Pre-Construction Activiti**	**121 days**	**Wed 11/16/11**	**Wed 5/2/12**		
54		Procure Professional S	40 days	Wed 11/16/11	Tue 1/10/12		
55		Procure Professional S	40 days	Wed 11/16/11	Tue 1/10/12		
56		Prequalify General Co	20 days	Thu 12/1/11	Wed 12/28/11		
57		Advertisement Numbe	5 days	Wed 3/21/12	Tue 3/27/12	52,56	
58		Advertisement Numbe	5 days	Wed 3/28/12	Tue 4/3/12	57	
59		Pre-bid Conference	1 day	Wed 4/4/12	Wed 4/4/12	58	
60		Bid Day	1 day	Thu 4/12/12	Thu 4/12/12	59FS+5 days	
61		Bid Review & Award	14 days	Fri 4/13/12	Wed 5/2/12	60	
62		**Construction Period**	**434 days**	**Thu 5/3/12**	**Tue 12/31/13**	61	
63		Notice to Proceed	1 day	Thu 5/3/12	Thu 5/3/12		
64		Interim Housing Consi	100 days	Fri 5/4/12	Thu 9/20/12	63	
65		New Edna Maguire Co	300 days	Wed 6/13/12	Tue 8/6/13		
66		Remove Interim Hous	105 days	Wed 8/7/13	Tue 12/31/13	65	
67							
68		**Tam. Valley, Old Mill, Middle S**	**464 days**	**Fri 2/12/10**	**Tue 11/22/11**		
69	✓	**District Programming**	**161 days**	**Fri 2/12/10**	**Thu 9/23/10**		
70	✓	Kick -off Meeting with	1 day	Wed 2/24/10	Wed 2/24/10		
71	✓	Ed. Spec review meet	1 day	Fri 2/12/10	Fri 2/12/10		
72	✓	Develop Design Comr	10 days	Thu 2/25/10	Wed 3/10/10		
73	✓	Procure Professional S	22 days	Thu 2/25/10	Fri 3/26/10		

Project: MVSC Master Bond Schedule
Date: Wed 10/26/11

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names
74	✓	Procure Professional S	22 days	Mon 2/22/10	Tue 3/23/10		
75	✓	CEQA Neg. Declaratic	1 day	Mon 5/3/10	Mon 5/3/10		
76	✓	Adopt Prequalification	40 days	Sun 8/1/10	Thu 9/23/10		
77	✓	**Schematic Design**	**71 days**	**Tue 3/9/10**	**Tue 6/15/10**		
78	✓	Develop Schematic D	60 days	Tue 3/9/10	Mon 5/31/10		
79	✓	District Review & Appr	12 days	Mon 5/31/10	Tue 6/15/10	78	
80	✓	**Design Development**	**66 days**	**Wed 6/16/10**	**Tue 9/14/10**		
81	✓	Develop DD Documer	55 days	Wed 6/16/10	Mon 8/30/10	79	
82	✓	District Review & Appr	11 days	Tue 8/31/10	Tue 9/14/10	81	
83	✓	**Construction Documents**	**43 days**	**Wed 9/15/10**	**Fri 11/12/10**		
84	✓	Develop 50% CD Doc	14 days	Wed 9/15/10	Mon 10/4/10	82	
85	✓	Develop 100% CD Do	20 days	Tue 10/5/10	Mon 11/1/10	84,84	
86	✓	District Review & Appr	9 days	Tue 11/2/10	Fri 11/12/10	85	
87	✓	**Agency Approval**	**209 days**	**Tue 6/1/10**	**Thu 3/17/11**		
88	✓	CDE Approval	20 days	Tue 6/1/10	Mon 6/28/10		
89	✓	DSA Approval	67 days	Mon 11/15/10	Tue 2/15/11	86	
90	✓	PM/CM Constructabili	67 days	Mon 11/15/10	Tue 2/15/11		
91	✓	Incorporate PM/CM &	5 days	Wed 2/16/11	Tue 2/22/11	90	
92	✓	DSA Backcheck	16 days	Wed 2/23/11	Wed 3/16/11	91	
93	✓	Final DSA Approval	1 day	Thu 3/17/11	Thu 3/17/11	92	
94	✓	**Pre-Construction Activiti**	**132 days**	**Mon 11/15/10**	**Tue 5/17/11**		
95	✓	Procure Professional S	30 days	Mon 11/15/10	Fri 12/24/10	86	
96	✓	Procure Professional S	44 days	Thu 3/17/11	Tue 5/17/11		
97	✓	Prequalify General Co	30 days	Tue 2/1/11	Mon 3/14/11		
98	✓	Advertisement Numbe	5 days	Tue 3/22/11	Mon 3/28/11	93	
99	✓	Advertisement Numbe	5 days	Tue 3/29/11	Mon 4/4/11	98	
100	✓	Pre-bid Conference	1 day	Thu 3/24/11	Thu 3/24/11		
101	✓	Bid Period	15 days	Fri 3/18/11	Thu 4/7/11	93	
102	✓	Bid Review & Award	14 days	Fri 4/8/11	Wed 4/27/11	101	
103		**Construction Period**	**149 days**	**Thu 4/28/11**	**Tue 11/22/11**		
104	✓	Notice to Proceed	1 day	Thu 4/28/11	Thu 4/28/11	102	
105	✓	Procurement Period	29 days	Fri 4/29/11	Wed 6/8/11	104	
106		Construction Period	114 days	Thu 6/9/11	Tue 11/15/11	105	
107		Closeout	5 days	Wed 11/16/11	Tue 11/22/11	106	
108							
109		**Park & Strawberry Point Elem**	**416 days**	**Mon 3/7/11**	**Mon 10/8/12**		
110		**Schematic Design**	**57 days**	**Mon 3/7/11**	**Tue 5/24/11**		
111		Develop Schematic D	38 days	Mon 3/7/11	Wed 4/27/11		
112		District Review & Appr	19 days	Thu 4/28/11	Tue 5/24/11	111	
113		**Design Development**	**46 days**	**Wed 5/25/11**	**Wed 7/27/11**		
114		Develop DD Documer	35 days	Wed 5/25/11	Tue 7/12/11	112	
115		District Review & Appr	11 days	Wed 7/13/11	Wed 7/27/11	114	
116		**Construction Documents**	**73 days**	**Thu 7/28/11**	**Mon 11/7/11**		
117		Develop 50% CD Doc	20 days	Thu 7/28/11	Wed 8/24/11	115	
118		District Review & Appr	15 days	Thu 8/25/11	Wed 9/14/11	117	
119		Develop 100% CD Do	28 days	Thu 9/15/11	Mon 10/24/11	118	
120		District Review & Appr	10 days	Tue 10/25/11	Mon 11/7/11	119	
121		**Agency Approval**	**95 days**	**Tue 11/8/11**	**Mon 3/19/12**		
122		CDE Approval	20 days	Tue 11/8/11	Mon 12/5/11	120	
123		DSA Approval	85 days	Tue 11/8/11	Mon 3/5/12	120	
124		PM/CM Constructabili	85 days	Tue 11/8/11	Mon 3/5/12	120	
125		Incorporate PM/CM &	10 days	Tue 3/6/12	Mon 3/19/12	124	
126		**Pre-Construction Activiti**	**165 days**	**Thu 9/15/11**	**Wed 5/2/12**		
127		DSA Backcheck	20 days	Tue 3/20/12	Mon 4/16/12	125	
128		Final DSA Approval	1 day	Tue 4/17/12	Tue 4/17/12	127	
129		Procure Professional S	30 days	Tue 11/8/11	Mon 12/19/11	120	
130		Procure Professional S	30 days	Thu 9/15/11	Wed 10/26/11	118	
131		Advertisement Numbe	5 days	Wed 4/18/12	Tue 4/24/12	128	
132		Advertisement Numbe	5 days	Wed 4/25/12	Tue 5/1/12	131	
133		Pre-bid Conference	1 day	Wed 5/2/12	Wed 5/2/12	132	
134		**Construction Period**	**113 days**	**Thu 5/3/12**	**Mon 10/8/12**		
135		Bid Day	1 day	Thu 5/3/12	Thu 5/3/12	133	
136		Bid Review & Award	10 days	Fri 5/4/12	Thu 5/17/12	135	
137		Notice to Proceed	1 day	Fri 5/18/12	Fri 5/18/12	136	
138		Procurement Period	22 days	Mon 5/21/12	Tue 6/19/12	137	
139		Construction Period	49 days	Wed 6/20/12	Mon 8/27/12	138	
140		Closeout	30 days	Tue 8/28/12	Mon 10/8/12	139	

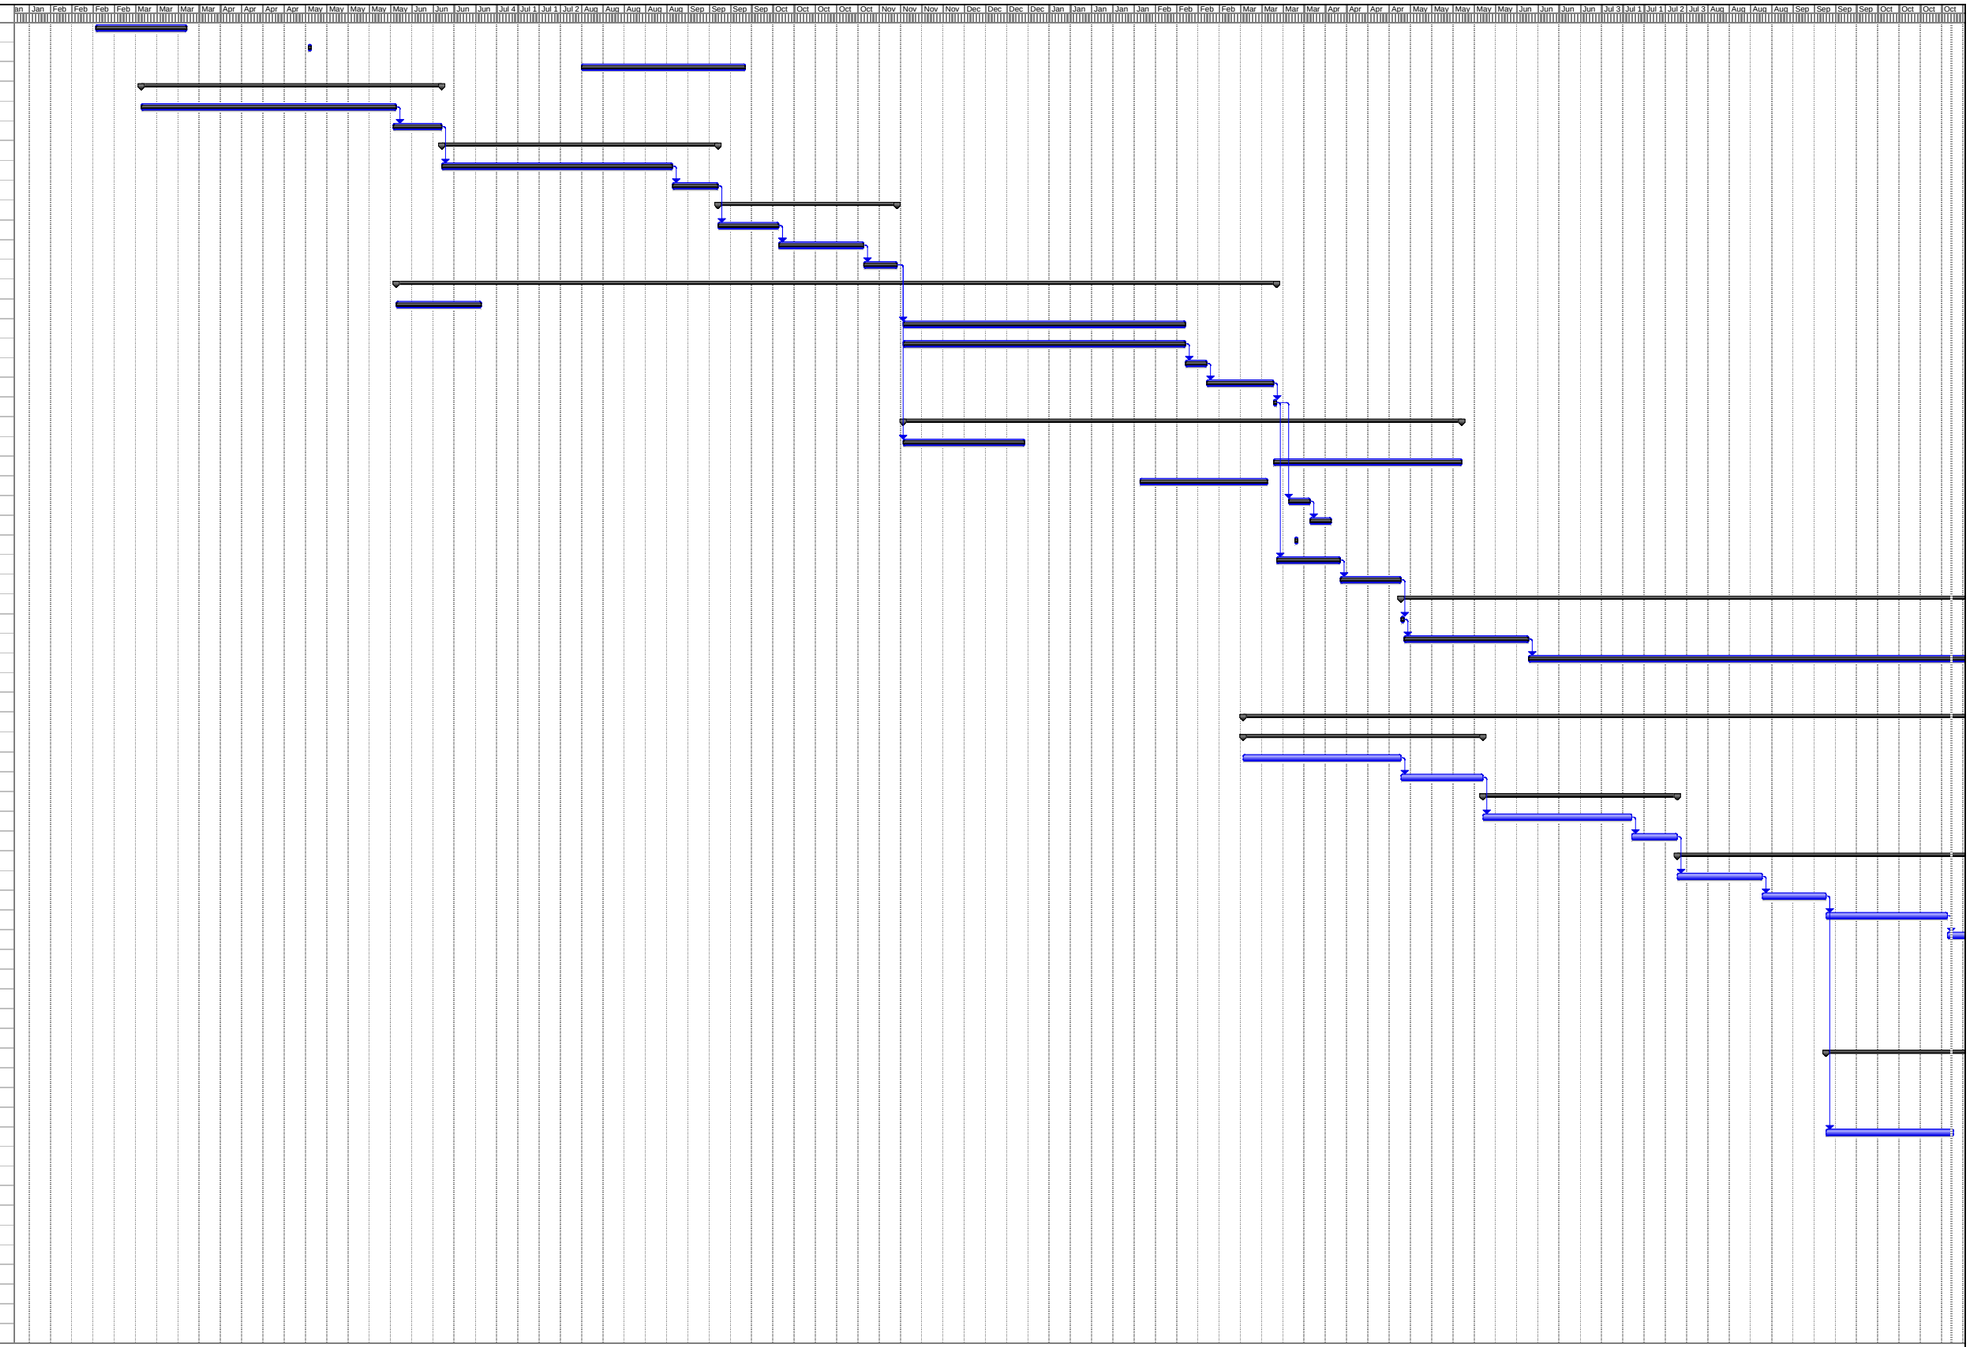

Project: MVSC Master Bond Schedule
Date: Wed 10/26/11

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

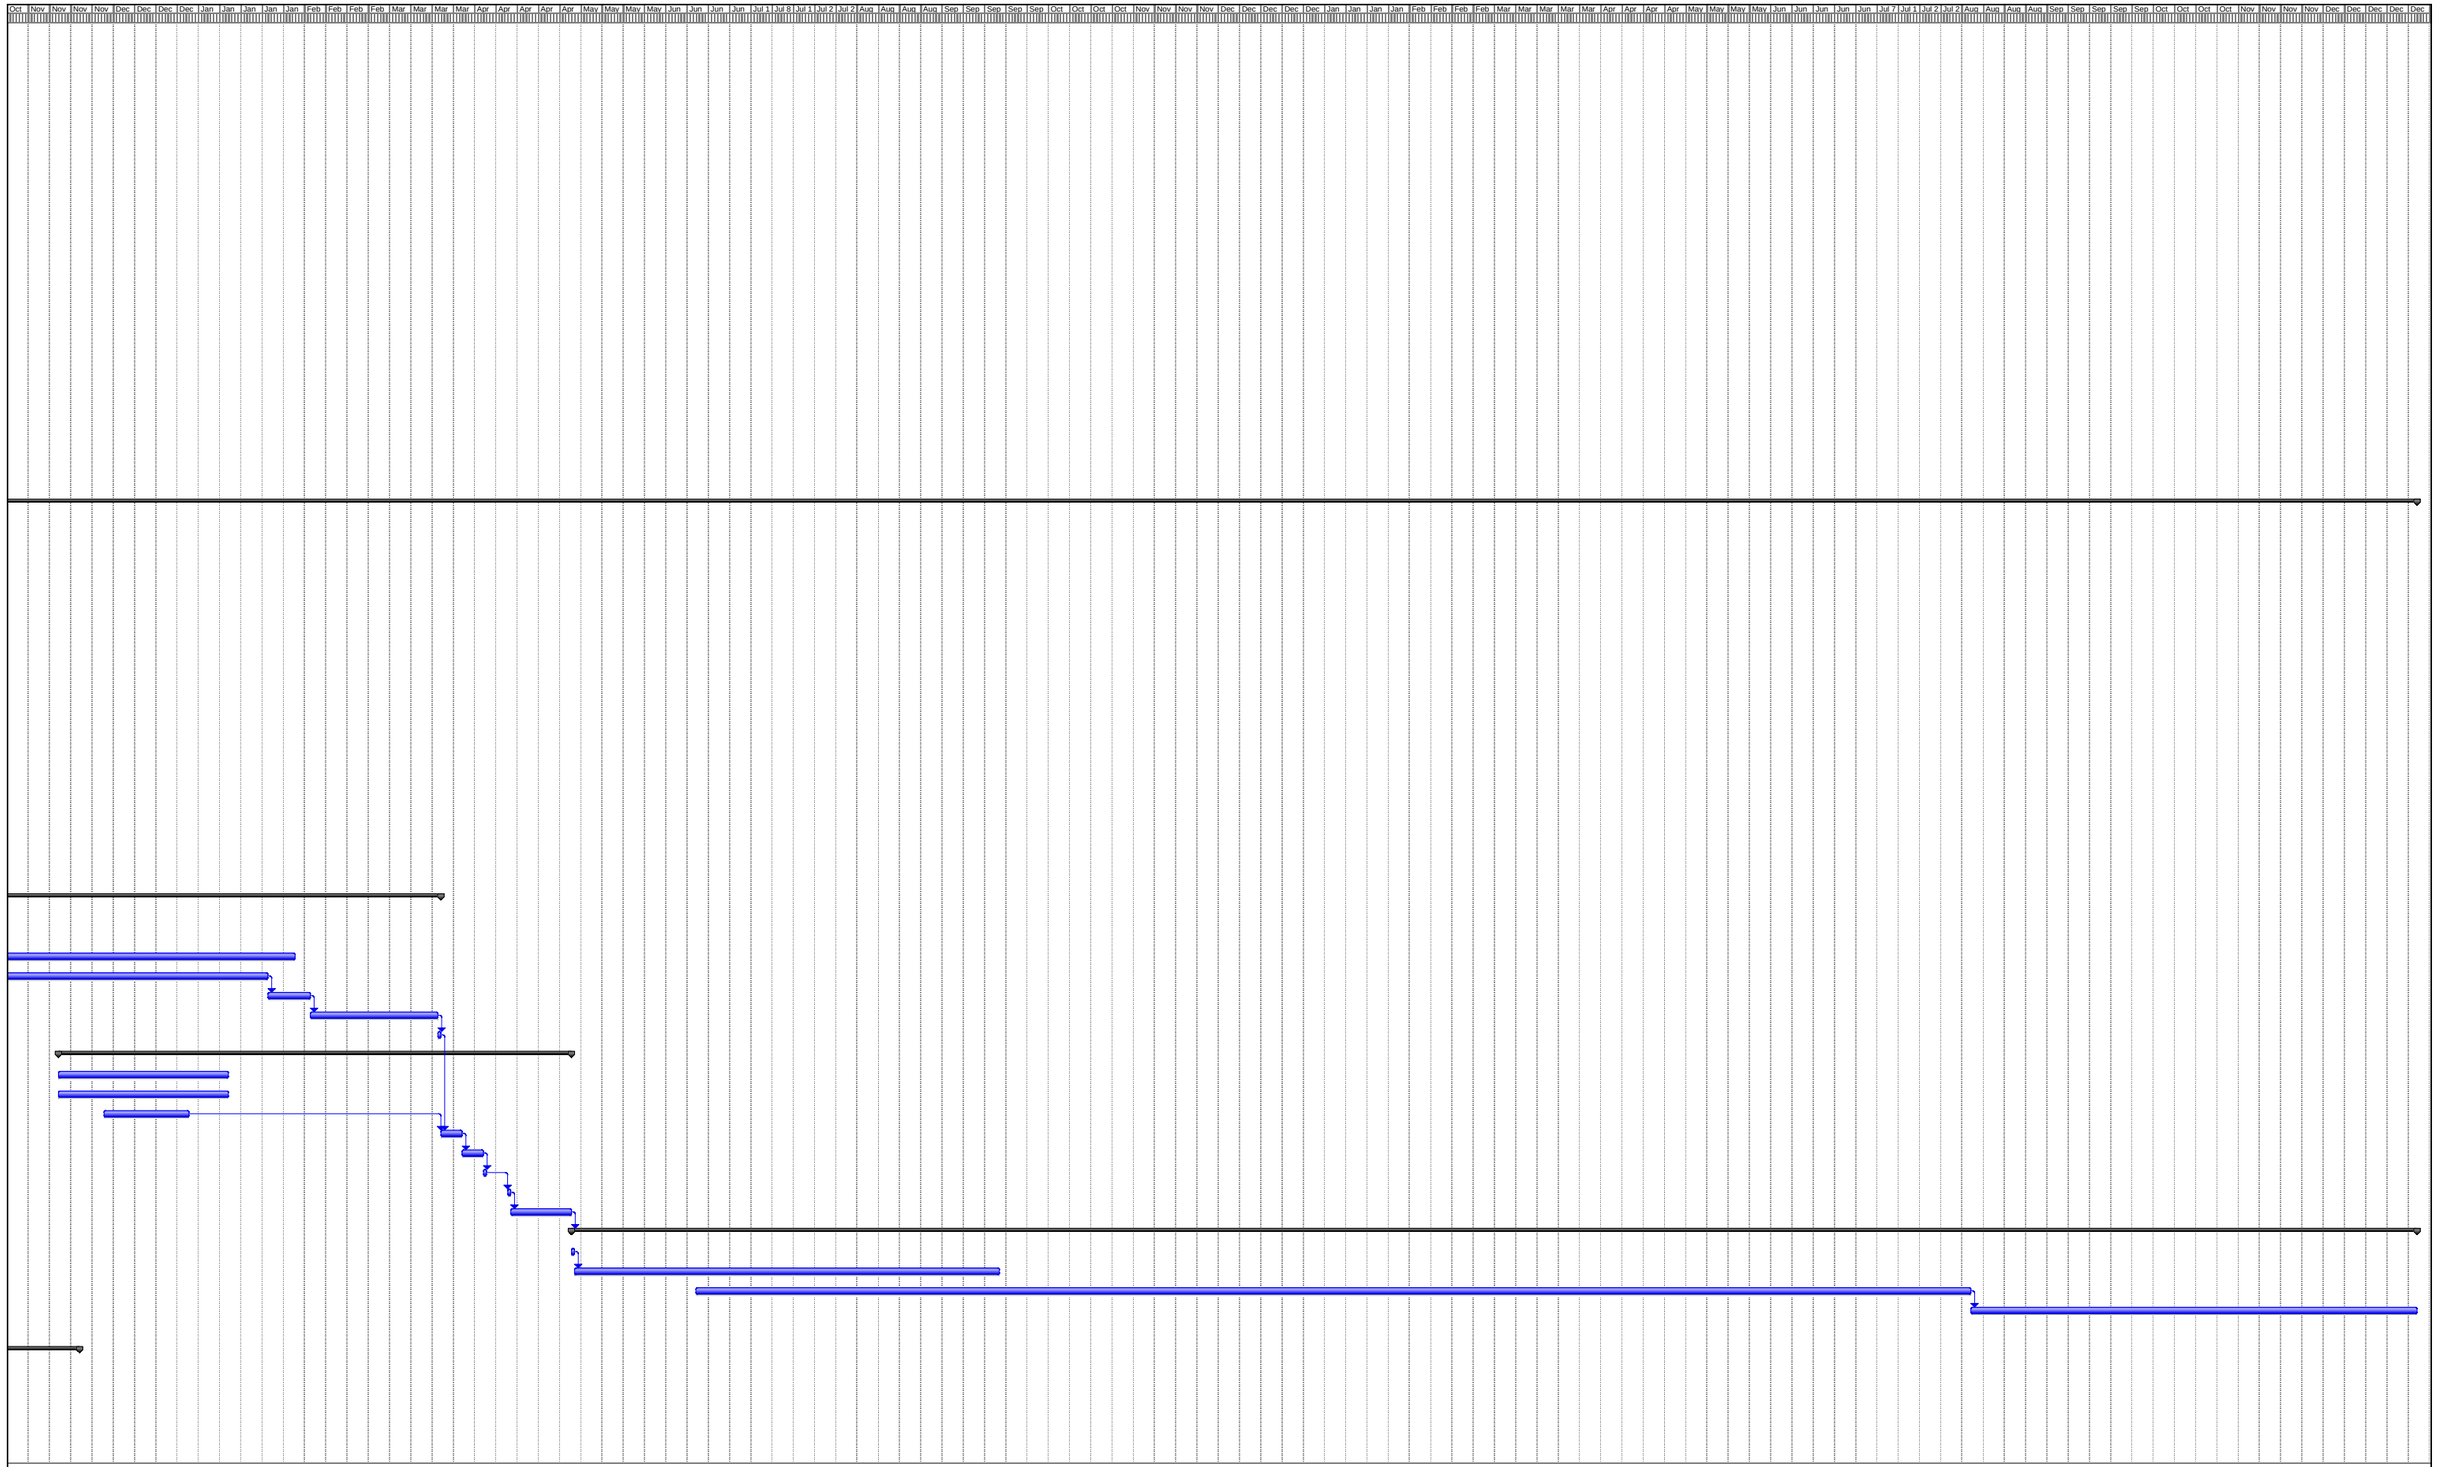

Project: MVSC Master Bond Schedule
Date: Wed 10/26/11

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

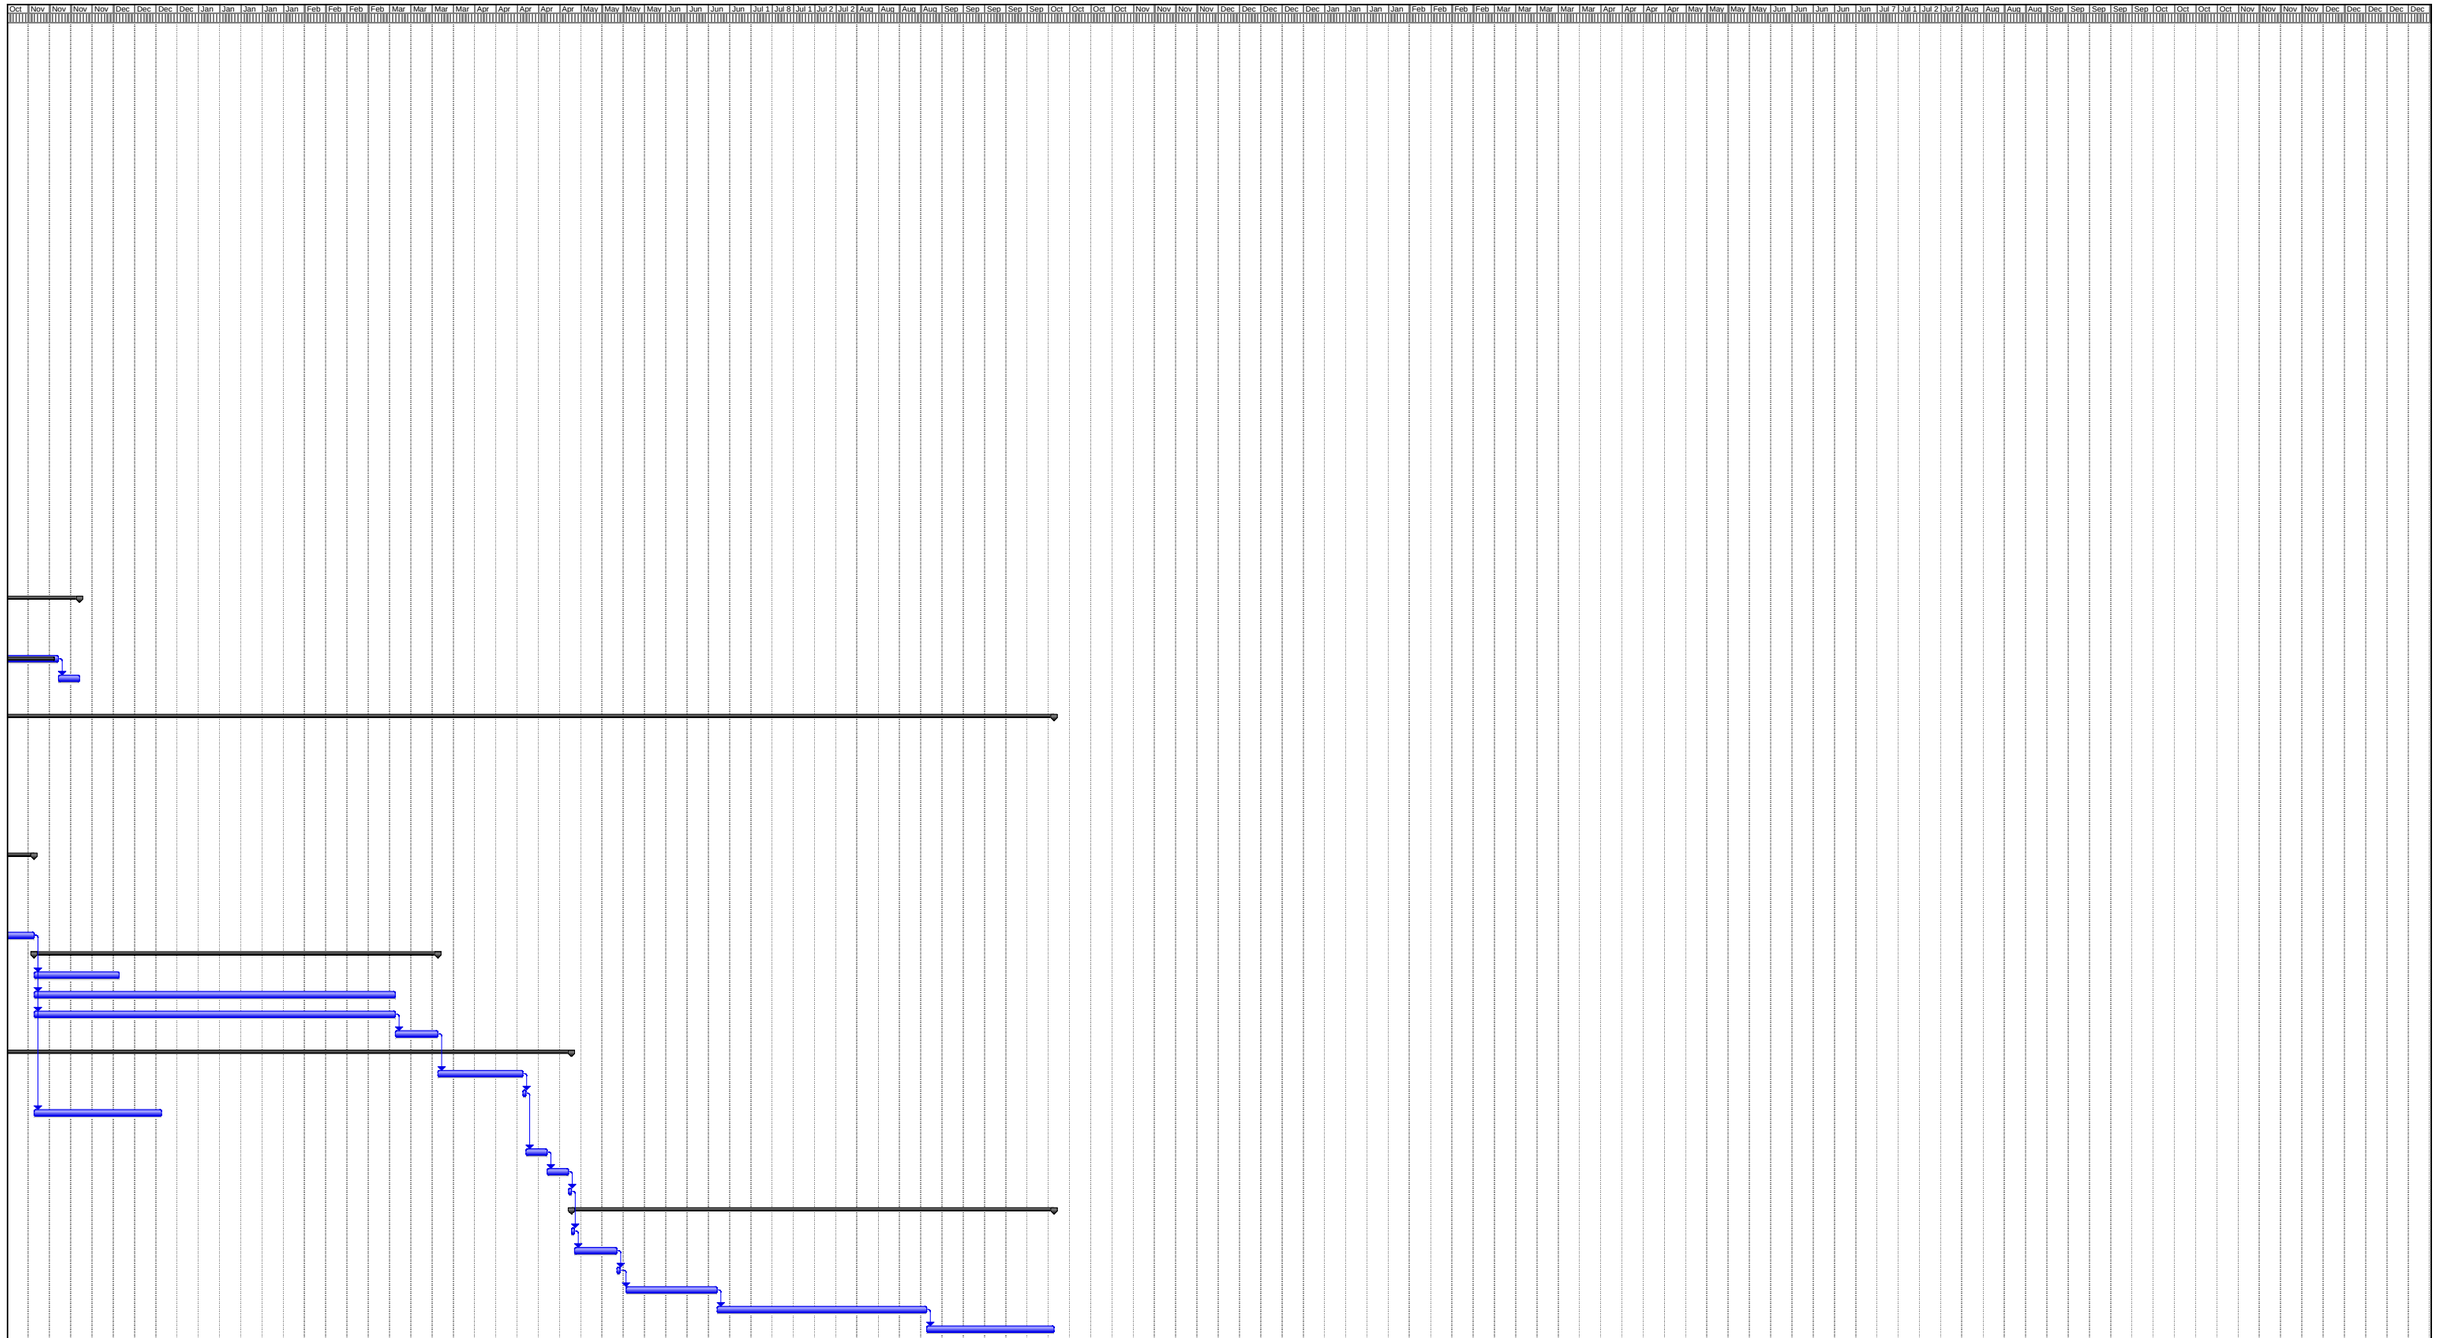

Project: MVSC Master Bond Schedule
Date: Wed 10/26/11

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
